



NH-44

TRAFFIC MANAGEMENT PLAN

REPORT ID

TMP-21PMG5P34

1 ZONE

PROJECT DETAILS

Project Name

NH-44

Client / Owner

1

Contractor

—

Permit No.

6

Total Zones

1

Work Zones

Zone 1

DOCUMENT INFO

Report ID

TMP-21PMG5P34

Generated

08 May 2026

Time

08:24 pm

Total Assets

18

Start Date

2026-05-08

End Date

2026-05-10

MAP LEGEND

 Traffic Cone

 Barrier / Board

 TMA Truck

 Sign / Signal

ZONE INDEX



50km/h · Lane · 18 assets · Boundary set

Zone 1

PROJECT RESOURCE AGGREGATION (FLEET OVERVIEW)

TOTAL EQUIPMENT ROLL-OUT

Aggregated requirement across all 1 work zones

EQUIPMENT CATEGORY	TOTAL QTY
Traffic Cones	16
Road Work Ahead Signs	1
TMA Trucks	1

SITE LOGISTICS & PROTOCOL

DEPLOYMENT GUIDELINES

- All equipment must be inspected for reflectivity and battery life (if applicable) prior to deployment.
- Cones and barriers should be placed in the downstream-to-upstream direction for setup safety.
- TMA trucks must be the first items placed and last items removed from the live carriageway.
- Site supervisors must verify all sign placements against the site map before active work commences.

ZONE: Zone 1 — SITE MAP & GEOMETRY

PATH LENGTH

308 m

FOOTPRINT

N/A

COMPLIANCE

PASS

CENTROID LAT

28.61432°

CENTROID LNG


77.20896°

TOTAL ASSETS


18

Speed: 50km/h · WZ Speed: 30km/h · Lanes: 2x3.5m · Surface: Asphalt · Closure: Lane · Spacing: 18 m

SITE MAP — AERIAL VIEWS

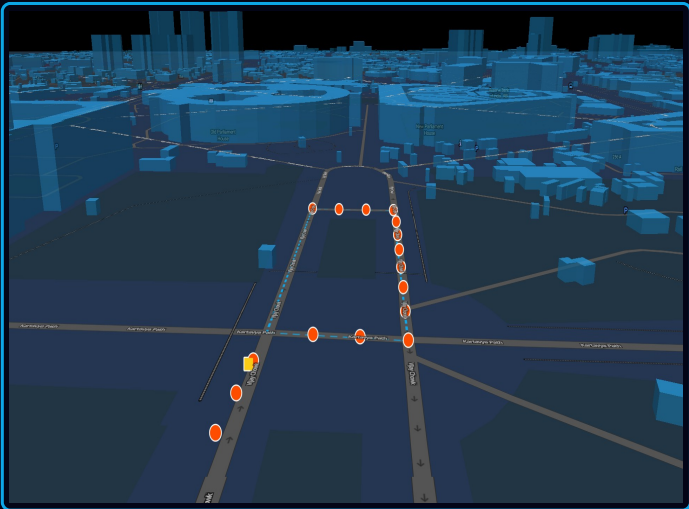


AERIAL: DARK PLAN

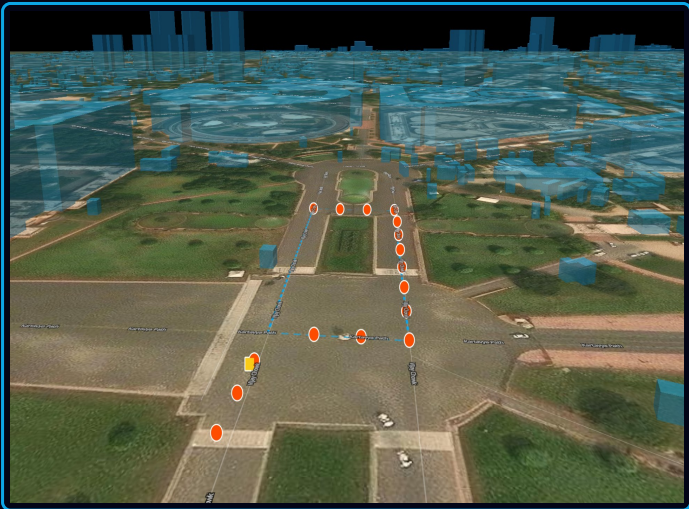


AERIAL: SATELLITE HD

SITE MAP — PERSPECTIVE VIEWS (3D)

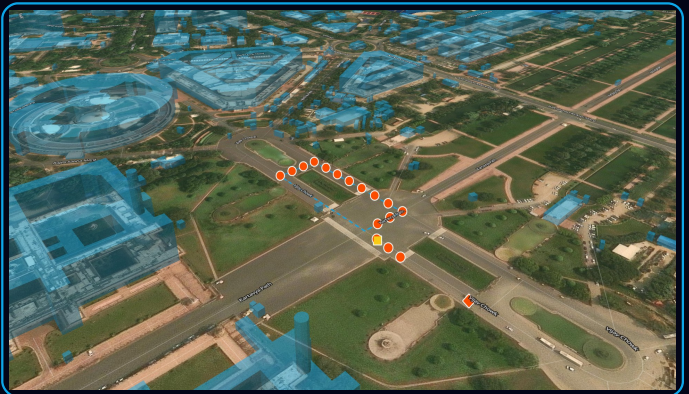

3D ISOMETRIC (AERIAL)

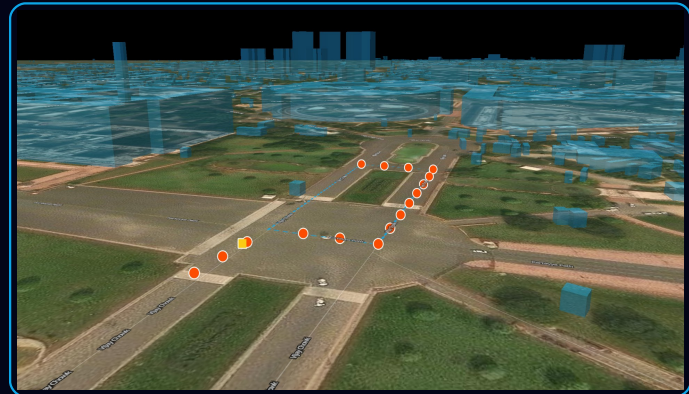

DRIVER APPROACH (GROUND)

ZONE: Zone 1 — EQUIPMENT MANIFEST

18

Total equipment items — Zone 1
Speed: 50km/h · Risk: MEDIUM · 08 May 2026

EQUIPMENT TYPE	PURPOSE	IRC STANDARD	QTY
Traffic Cones types: cone · unit: EA	Perimeter delineation and lane channelisation	Space at calculated intervals per speed limit (IRC SP 55)	16
Road Work Ahead Signs types: sign-roadwork · unit: EA	Advance warning to approaching traffic of work zone	Position at minimum advance warning distance upstream	1
Lane Merge Signs types: sign-merge · unit: EA	Warn drivers of lane reduction and required merge	Install before taper start; repeat at mid-taper if >50 m	—
Slow Down Signs types: sign-slow · unit: EA	Speed reduction advisory on approach to work zone	Space at 50 m intervals; minimum 2 signs per approach	—
Detour Signs types: sign-detour · unit: EA	Route diversion guidance for diverted road users	Install at all junction approaches on nominated detour route	—
Water-Filled Barriers types: barrier · unit: EA	Physical separation and impact protection between traffic and workers	Deploy at high-risk sections; anti-ram couplings (IRC §6.4)	—
TMA Trucks types: truck · unit: EA	Truck-mounted attenuator — rear impact protection for work crew	Position at tail of zone facing oncoming traffic	1
Signal / Light Points types: sign · unit: EA	Temporary traffic signal control at zone entry and exit	Min 75 m sight distance to signal head (IRC §8.3)	—
Flaggers types: flagger · unit: PERSON	Manual traffic control at zone boundaries during active work	Stop/slow paddle per IRC §7.2; radio comms mandatory	—
Site Supervisors types: supervisor · unit: PERSON	On-site safety compliance oversight and incident response	Min 1 supervisor per 200 m of active zone (IRC §5.1)	—

TOTAL — ZONE 1

18

SAFETY PARAMETERS (IRC SP 55:2014)

Zone 150km/h · Taper: 40 m · Spacing: 18 m · Adv Warning: 100 m · Risk: MEDIUM · Closure: Lane

PROJECT & PERSONNEL

Project Name	Permit / Auth. No.
NH-44	6
Client / Owner	Contractor
1	—
Superintendent	Safety Officer
thekedaar	prashant
Emergency Tel.	Night Works
91+ 9650912914	No
Work Period	Working Hours
2026-05-08 to 2026-05-10	07:00–17:00

APPROVAL & SIGN-OFF

SITE SUPERINTENDENT	SAFETY OFFICER	AUTHORITY APPROVAL
thekedaar	prashant	Road authority / Municipal corporation rep.
On-site execution and equipment deployment	IRC SP 55 compliance verification authority	
Signature	Signature	Signature
Full Name & Designation	Full Name & Designation	Full Name & Designation
Date: 08 May 2026	Date: 08 May 2026	Date: 08 May 2026
